


| ID | Task Name | Duration | Start | Finish | Nov '04 | | | | | | | 06 Dec '04 | | | | | | | 13 Dec '04 | | | | | | | 20 Dec '04 | | | | | | | 27 Dec '04 | | | | | | | 03 Jan '05 | | | | | | |
|----|---|--------------------|---------------------|---------------------|---------|---|---|---|---|---|---|------------|---|---|---|---|---|---|------------|---|---|---|---|---|---|------------|---|---|---|---|---|---|------------|---|---|---|---|---|---|------------|---|---|--|--|--|--|
| | | | | | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | | | | |
| 1 | Design Specification | 5 days | Wed 01/12/04 | Tue 07/12/04 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 2 | Write Design Specification | 5 days | Wed 01/12/04 | Tue 07/12/04 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 3 | PCB Design | 45.65 days | Thu 09/12/04 | Mon 21/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 4 | Parts investigation | 2.5 days | Thu 09/12/04 | Mon 13/12/04 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 5 | Design spec changes | 1.25 days | Mon 13/12/04 | Tue 14/12/04 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 6 | Schematic Capture | 5 days | Tue 14/12/04 | Wed 22/12/04 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 7 | Footprint Creation | 0.94 days | Wed 22/12/04 | Thu 23/12/04 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 8 | Footprint Checking | 0.25 days | Thu 23/12/04 | Tue 04/01/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 9 | PCB Outline | 0.62 days | Tue 04/01/05 | Tue 04/01/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 10 | PCB Height restraints | 0.31 days | Wed 05/01/05 | Wed 05/01/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 11 | Component Placement | 1.25 days | Wed 05/01/05 | Thu 06/01/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 12 | Design rule input | 0.31 days | Fri 07/01/05 | Fri 07/01/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 13 | Routing | 2.5 days | Fri 07/01/05 | Wed 12/01/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 14 | Post Route Clean-up | 0.31 days | Wed 12/01/05 | Wed 12/01/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 15 | BOM | 0.5 days | Wed 12/01/05 | Thu 13/01/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 16 | Documentation | 2.5 days | Thu 13/01/05 | Mon 17/01/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 17 | Prototype fire up | 2.5 days | Tue 01/02/05 | Fri 04/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 18 | Protoype testing | 2.5 days | Fri 04/02/05 | Tue 08/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 19 | Test Rig & procedure | 3.75 days | Tue 08/02/05 | Tue 15/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 20 | Production Turn Schematic & Bom Changes | 1.75 days | Tue 15/02/05 | Thu 17/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 21 | Production Turn PCB Layout | 2 days | Thu 17/02/05 | Mon 21/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 22 | Design reviews | 47.15 days | Wed 08/12/04 | Tue 22/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 23 | Internal Design Specification review | 0.5 days | Wed 08/12/04 | Wed 08/12/04 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 24 | Design Specification review | 0.5 days | Wed 08/12/04 | Wed 08/12/04 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 25 | Internal schematic review | 0.5 days | Fri 17/12/04 | Fri 17/12/04 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 26 | schematic review | 0.5 days | Wed 22/12/04 | Wed 22/12/04 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 27 | PCB outline review | 0.5 days | Tue 04/01/05 | Wed 05/01/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 28 | PCB placement review | 0.5 days | Thu 06/01/05 | Fri 07/01/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 29 | PCB routing review | 0.5 days | Wed 12/01/05 | Wed 12/01/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 30 | Project review | 0.5 days | Mon 21/02/05 | Tue 22/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 31 | Prototype Manufacture | 20.85 days? | Tue 04/01/05 | Tue 01/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 32 | PCB Manufacture | 5 days | Mon 17/01/05 | Mon 24/01/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 33 | Prototypes Parts Procurement | 3 days | Tue 04/01/05 | Mon 17/01/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 34 | Kit Check & Machine setup at PCB Assy Hse | 1 day? | Mon 24/01/05 | Tue 25/01/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 35 | PCB Assembly | 5 days | Tue 25/01/05 | Tue 01/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 36 | Assembly & Testing | 6 days | Tue 08/02/05 | Wed 16/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 37 | Unit Assembly | 1 day | Tue 08/02/05 | Wed 09/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 38 | Mechanical Testing | 1 day | Wed 09/02/05 | Thu 10/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 39 | Functional Testing | 2 days | Thu 10/02/05 | Mon 14/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 40 | Compliance Testing | 2 days | Mon 14/02/05 | Wed 16/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 41 | Ready for Manufacture | 0 days | Mon 21/02/05 | Mon 21/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 42 | Documentation | 8 days | Wed 16/02/05 | Mon 28/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 43 | Write User Manual | 3 days | Wed 16/02/05 | Mon 21/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 44 | Write Installation Manual | 1 day | Mon 21/02/05 | Tue 22/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 45 | Write OS installation manual(s) | 4 days | Tue 22/02/05 | Mon 28/02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

Project: Mid-Range Panel PC
Document Number: 108-001
Date: Fri 24/06/05

| | | | | | | | | | |
|-------|--|-----------|--|-----------------|--|--------------------|--|----------|--|
| Task | | Progress | | Summary | | External Tasks | | Deadline | |
| Split | | Milestone | | Project Summary | | External Milestone | | | |

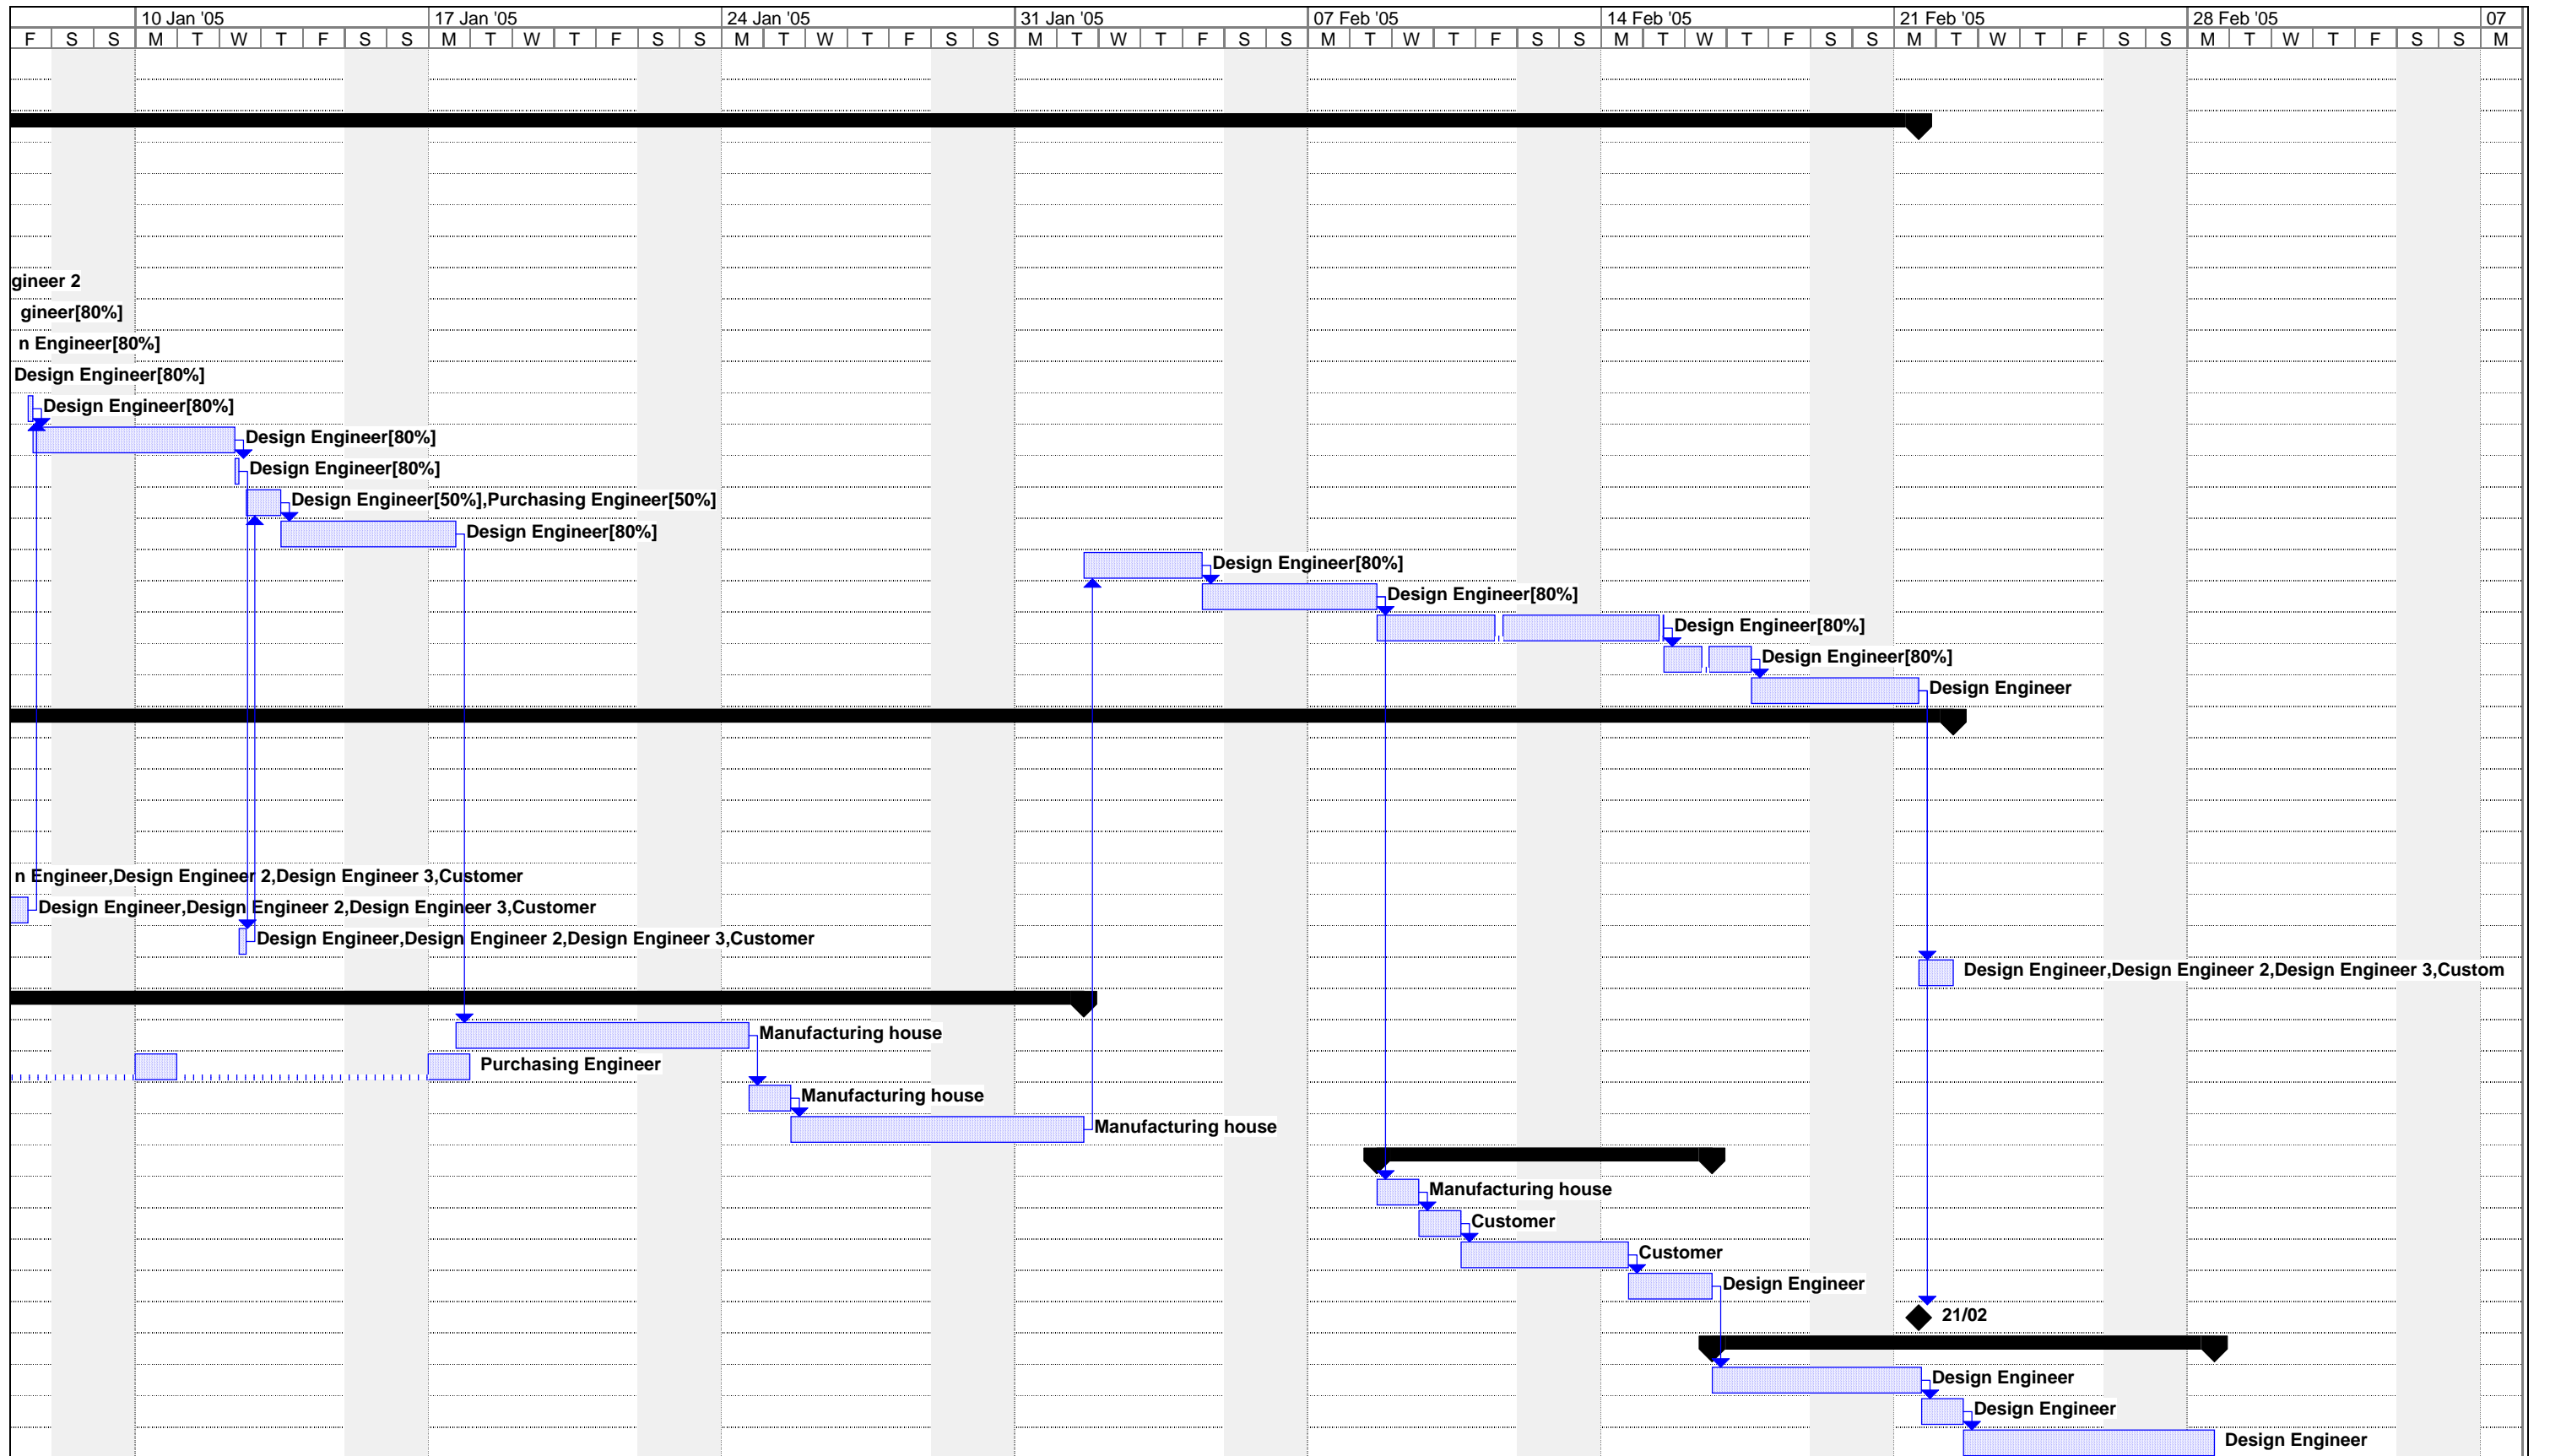

Project: Mid-Range Panel PC
 Document Number: 108-001
 Date: Fri 24/06/05

| | | | | | | | | | |
|-------|--|-----------|--|-----------------|--|--------------------|--|----------|--|
| Task | | Progress | | Summary | | External Tasks | | Deadline | |
| Split | | Milestone | | Project Summary | | External Milestone | | | |
